



#### University Construction Oversight Meeting

# Project Updates – University Construction / Operations

## Dr. Alan Robertson Vice President for Finance and Administration / CFO

#### Florida Agricultural and Mechanical University Board of Trustees



#### University Construction Oversight Meeting Friday, May 21, 2021 2:00 PM Conference Call

#### **AGENDA**

I. Call to Order
 III. Roll Call
 III. Opening Remarks
 IV. Major Capital Projects Updates:
 VP Robertson
 a. Student Amphitheater
 b. Bragg Memorial Stadium
 V. Questions

Trustee Moore

Adjournment


VI.


### Major Capital Projects Update

- Student Amphitheater
- ❖Bragg Memorial Stadium



### Student Amphitheater

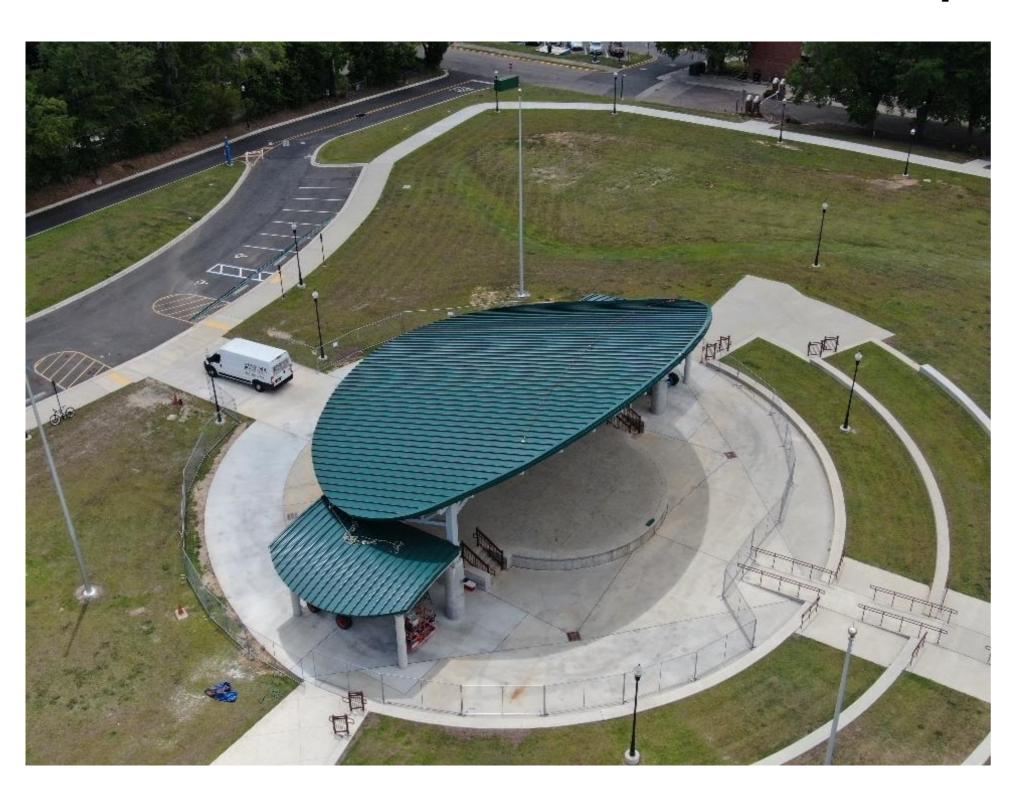

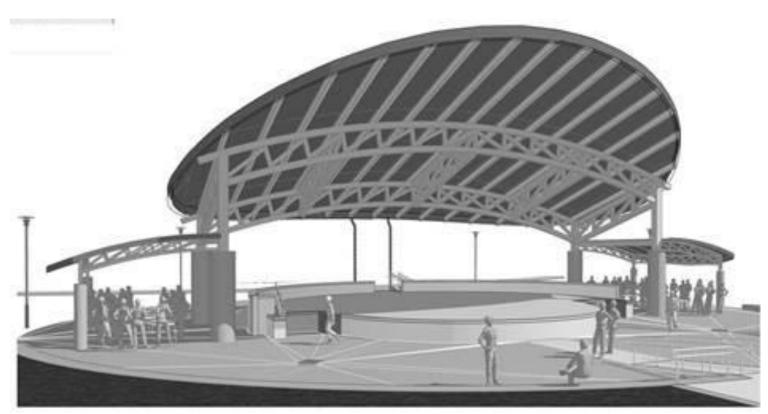

### Student Amphitheater

Project Status Repor	t: Budget: \$2,520,9	00 Date: 5/2		21/2021
Project #:	Project Name:	University Project Manager:		Project Status:
CITF 2019	Student Amphitheater	David Rosenfeld		
Design Status (% Complete):	Designer:	Substantial Completion Date:		
100%	GRC Architects	May 14, 2021		Revised Schedule
Construction Status (% Complete)	: Contractor:	0	ccupancy Date:	
100%	RAM Construction		May 30, 2021	
Timely Completion Risk: Mitigation Strategy:	Severe weather and delivery of mater None	ials		
Project Contracts:	Expenses:	E	ncumbrances:	Remaining:
\$2,520,900	\$2,422,880	\$97,898		\$0

## Bragg Memorial Stadium FAMU FLORIDA AGRICULTURAL AND MECHANICAL UNIVERSITY










## Bragg Memorial Stadium FAMU FLORIDA AGRICULTURAL AND MECHANICAL UNIVERSITY



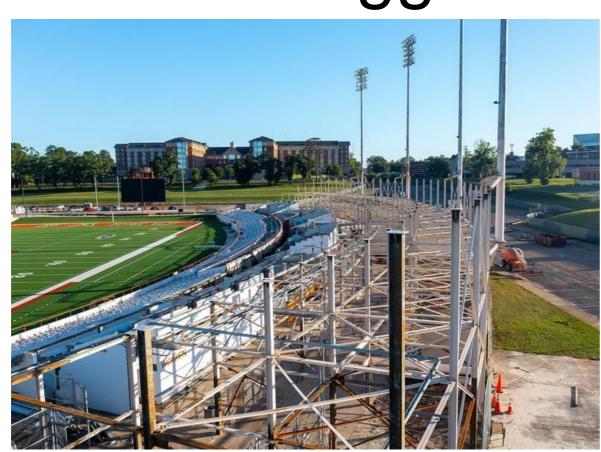





#### ESSENTIAL CONSTRUCTION SERVICES SCOPE OF WORK (PHASE I) \$4,000,000

- Remove steel pans and seating east side of stadium
- Repair structural steel east side of stadium
- Water blast steel frame and repaint east side of stadium
- Replace steal pans with aluminum pans east side of stadium
- Install new seating east side of stadium

#### Phase I - Bragg Memorial Stadium

Project Status Report:	Budget: \$4,000,0	0 Date: 5/2		1/2021	
Project #:	Project Name:	University Project Manager:		Project Status:	
BRFM 346	Bragg Stadium Renovation	Bodie young/Elston Peets			
Design Status (% Complete):	Designer:	Substantial Completion Date:			
95%	Barkley Engineering	Sep 11, 2021		Construction	
Construction Status (% Complete):	Contractor:	О	ccupancy Date:		
40%	Ram Construction		Sep 30, 2021		

Timely Completion Risk: Severe weather, material delays, COVID

Mitigation Strategy: Identifying critical path materials that could impact the schedule

Project Contracts:	Expenses:	Encumbrances:	Remaining:
\$3,718,561	\$267,583	\$3,450,978	\$281,439



"At FAMU, Great Things are Happening Every Day!"

