

University Construction Oversight Meeting



Florida Agricultural and Mechanical University Board of Trustees



University Construction Oversight Meeting Thursday, December 16, 2021 2:30 PM Conference Call

AGENDA

I. Call to Order Trustee Moore

II. Roll Call Dr. Turner

III. Opening Remarks Chair Lawson

IV. Major Capital Project Updates: Bragg Memorial Stadium VP Brown

V. Questions

VI. Adjournment Trustee Moore

Phase 2a - Bragg Memorial Stadium

Project Status Report:		Budget: \$8,000,000		Date: 12/16/2021	
Project #:		Project Name:	University Project Manager:		Project Status:
BRFM 346		Bragg Stadium Renovation	Bodie Yo	ung / David Rosenfeld	
Design Status (% Complete):		Designer:	Substan	tial Completion Date:	
100%	Clei	mons Rutherford & Associates		-	Design
Construction Status (% Complete):		Contractor:	00	ccupancy Date:	
15%		Allstate Construction, Inc.		-	

Timely Completion Risk: Severe weather, material delays, COVID

Mitigation Strategy: Identifying critical path materials that could impact the schedule

Project Contracts:	Expenses:	Encumbrances:	Remaining:
\$5,251,072	\$3,776,643.60	\$5,251,072	\$2,748,928


FAMU Bragg Stadium Phase 2a - Construction Activities



- Allstate Construction Inc. has begun operations to renovate the west side of Bragg Memorial Stadium.
- The preparation for demolition and securing the site is underway, with stripping the bleachers of all electrical, plumbing and lighting fixtures beginning immediately.



FAMU Bragg Stadium Phase 2a – Construction Activities

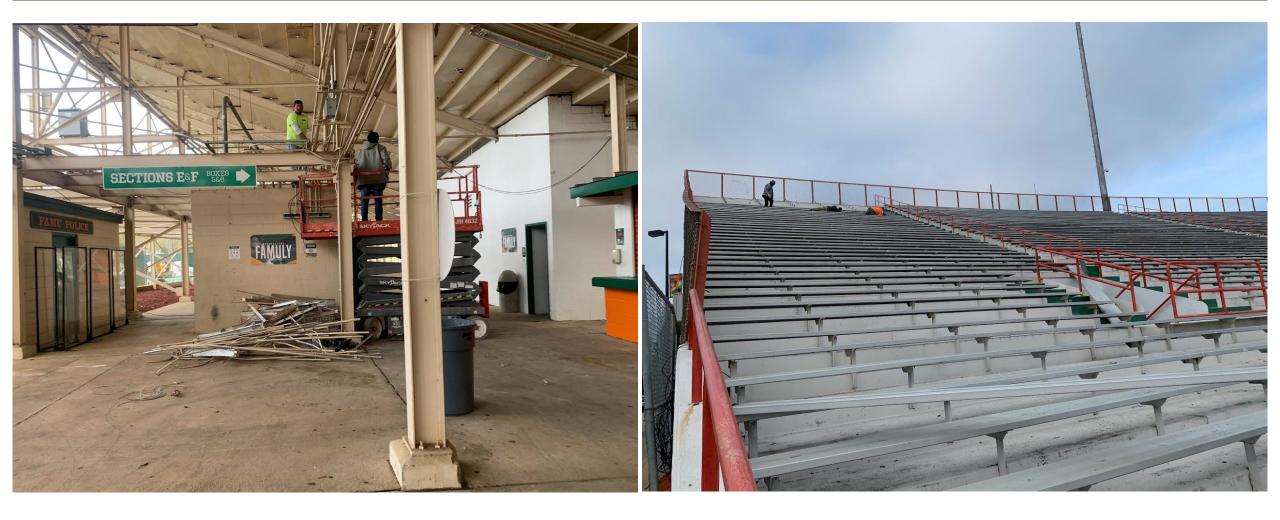

Subcontractors Disconnecting Existing Electrical.

• Subcontractors removing existing stadium aluminum benches To be stockpiled.

FAMU Bragg Stadium Phase 2a – Construction Activities






• Existing westside grandstands stadium aluminum bench seating removed in the first two sections of the stands.

• Subcontractors removed existing stadium aluminum bench seating and stockpiled.

FAMU Bragg Stadium Phase 2a – Action Item from Dec 2, 2021 BFF Committee Mtg

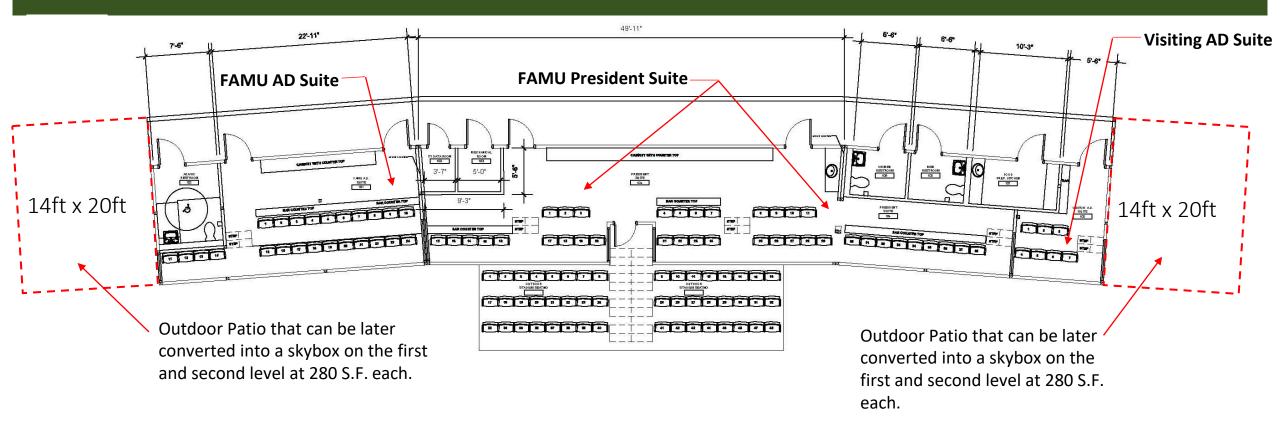

Additional Skybox Information

- Based on Phase 2A structure, 4 additional patios/skyboxes can be added at a later date.
- Proposed location of the skyboxes will be on both sides of President's suite.
- Each skybox will be approximately 280 S.F. Approximate cost per skybox is \$280,000., totaling \$1,120,000.
- Additional Restrooms will need to be added as the Occupancy count increases do to the skyboxes addition.

